



N E X T D C where the cloud lives®

Date: 04 February 2026

Department of Planning,
Housing and Infrastructure
12 Darcy Street
Parramatta NSW 2150

Attn: Christopher Ritchie, Shaun Williams and Joanna Bakopanos

Re: NEXTDC S4 (Phase 2) Scoping Meeting with Department

This letter serves as formal correspondence regarding the development application for NEXTDC S4 (Phase 2) Project [PDA-102095472]. Following our recent meeting on the 22nd of January 2026, we are providing the enclosed documentation to address the recycled water approach.

NEXTDC is pursuing a recycled water supply for the S4 Development to secure a resilient non-potable water source that reduces reliance on Sydney's potable water network, aligns with circular economy objectives, and supports the reliable operation of critical digital infrastructure in Western Sydney.

The recycled supply will service the site's non potable loads, primarily cooling and heat rejection systems that constitute the vast majority of site usage.

The scheme comprises a 10.5 km transfer pipeline from AquaNet's Smithfield network to Horsley Park, two high level reservoirs, and dual gravity transfer mains into S4. The recycled network can provide up to 16.8 ML/day with a peak flow of 192.1 L/s, dual asset redundancy and provision for an on-site booster should higher boundary pressure be required. The site's maximum demands remain 20.39 ML/day and 236 L/s; NEXTDC is investigating additional augmentation works and solutions to bridge this capacity gap.

This initiative falls under Part 5 of the EP&A Act where the Independent Pricing and Regulatory Tribunal (IPART) acts as the determining authority for the planning approval pathway. To support the approval process, a Review of Environmental Factors (REF) is required and is currently in progress. The REF includes assessments on land/soils and contamination, biodiversity, aboriginal cultural heritage, historic (non-aboriginal) heritage, noise and vibration, traffic/access and utilities, amenity and visual, air quality, water and flooding, waste and resources, hazard and risk including cumulative impacts, environmental management and mitigation, stakeholder and agency engagement. This process is underway with a targeted submission to IPART by end of February 2026 and the approval obtained by July 2026.

The program is advancing through design, approvals, procurement, and construction, targeting full operational readiness of the network extension in Q4 2027, following commissioning of the reservoirs, transfer pipeline, and associated controls. Authority engagement is ongoing to ensure compliance and schedule certainty.

NEXTDC looks forward to ongoing collaboration with the Department of Planning to deliver a reliable, sustainable recycled water solution that secures S4's needs and contributes to broader regional water security. The project provides a scalable model for high tech precincts transitioning to efficient, low impact utilities while maintaining the service reliability expected of essential digital infrastructure.



N E X T D C where the cloud lives®

We trust the attached information satisfies the query around the approach to the recycled water. Should you require further clarification, please do not hesitate to contact the undersigned.

For and behalf of NEXTDC,


Daniel Howard

Chief Development Officer, Hyperscale



N E X T D C where the cloud lives®

Pipeline route – Smithfield to reservoir

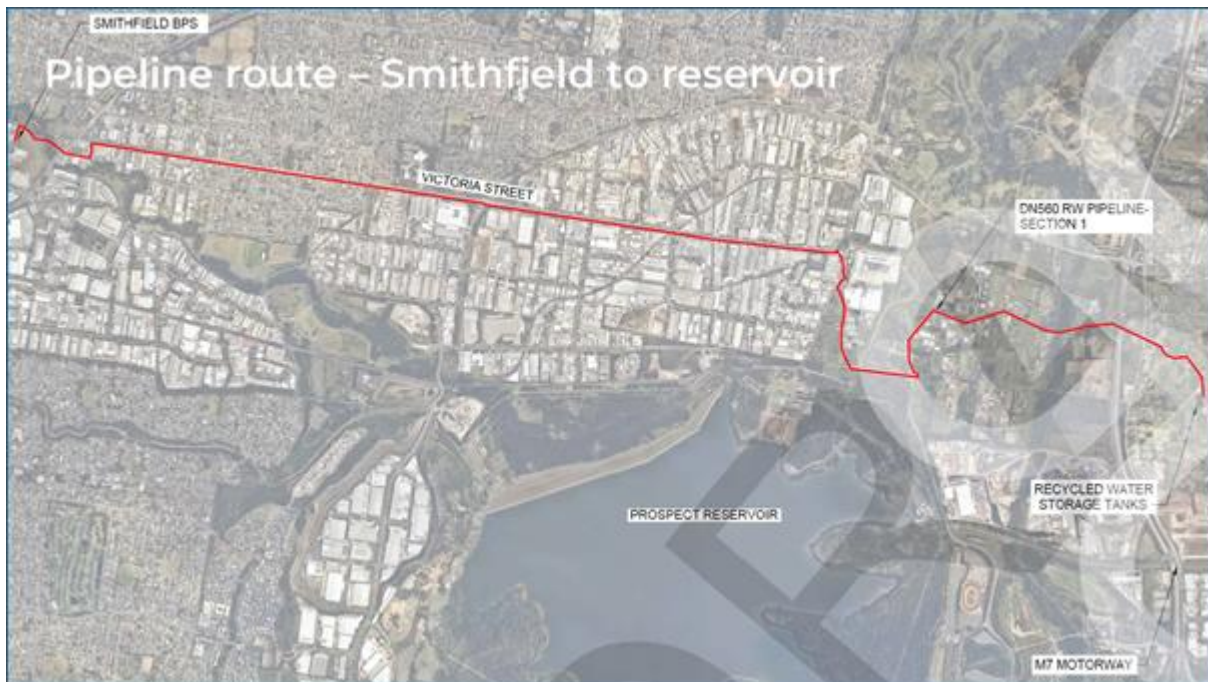

Pipeline route – Reservoir to NEXTDC site

