


NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Power & Water

**Lot 306 is also known on the planning portal as: PDA-102095472 | NEXTDC S4 (Phase 2) Data Centre Horsley Park*

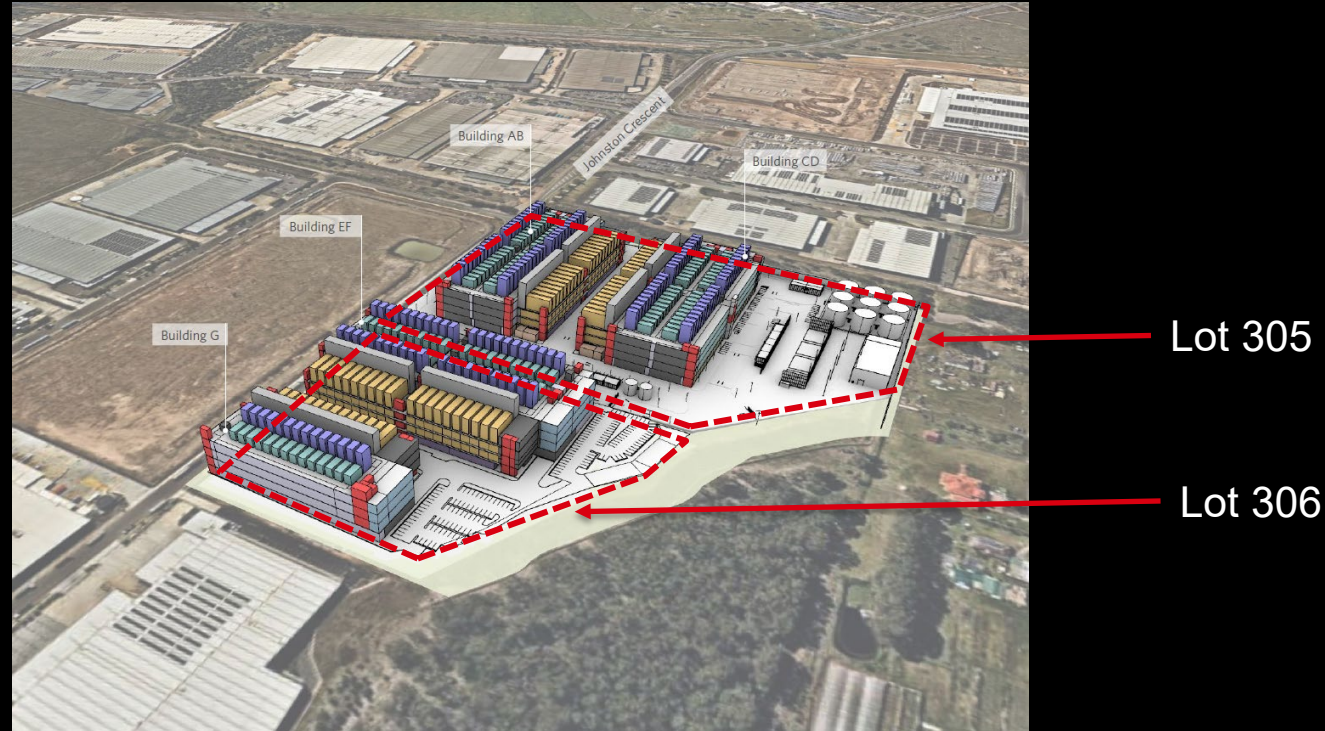

Lot 306 is an extension of Lot 305 (SSD-63741210 | NEXTDC S4 Data Centre Horsley Park). As such the overarching strategy is that **the majority of the utilities are also an extension from Lot 305**. The following pages notes the power and water strategy for servicing Lot 306.

NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Power

Power provision to Lot 306 via Transgrid Sydney West (through Lot 305)



Transgrid Sydney West site

Off Site Cabling Route

Lot 305

Lot 306

Within Lot 305

- 330kV substation (4 x Transformers with Acoustic wall)
- GIS Building
- 33kV switching station

Outside of Lot 305

- Cable route from Lot 305 to Sydney West site via Old Wallgrove Road, approx. 2.6km extending across 2 x LGAs – Fairfield and Blacktown.
- 2 x 330kV underground transmission cable circuit comprising three cables installed in three conduits.
- 2 x smaller conduits for optical fibres.

Within the Sydney West site

- Extension of the existing substation bench to enable the construction of 2 new 330kV feeder bays including moving of access road and moving of fence line.
- Extension to 330kV Busbar-B Section-2.
- Construction of 2 new 330kV switchbay and associated primary and secondary equipment.
- Construction of a new secondary systems building.

NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Power

Power Supply

Electricity will be supplied from the NEXTDC dedicated substation located on Lot 305, which receives power from the Transgrid Sydney West Substation via high-voltage underground transmission infrastructure.


The installed infrastructure provides a total electrical capacity of 500 MVA across the S4 campus.
The current allocation of electrical capacity across the campus is:

The proposed Lot 306 development has an estimated operational power consumption of approximately 134.4 MW, which is accommodated within the allocated electrical capacity.

The overall electrical demand across the campus remains within the installed transformer capacity and no additional electrical supply upgrades are required during the operational stage of the development.

Development	Allocated Capacity
Lot 305	308 MVA
Lot 306	192 MVA
Total Campus Capacity	500 MVA

Points of entry to Lot 306

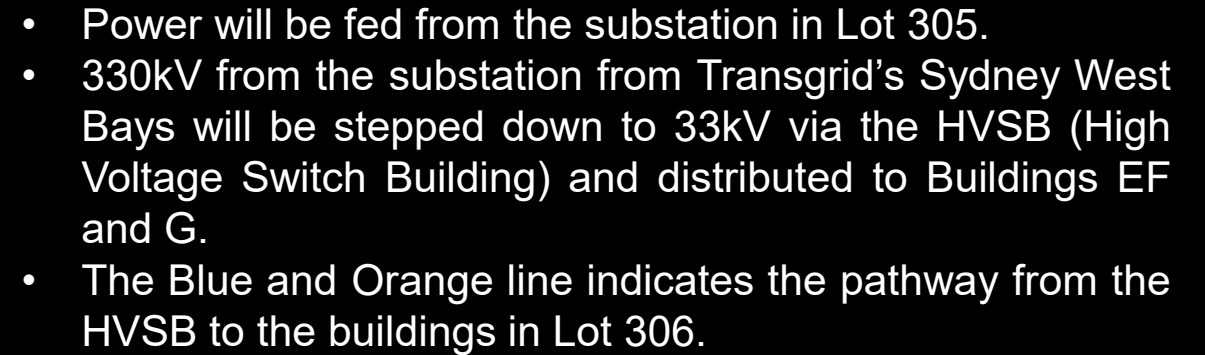

**all pathways indicated are conceptual only and further design development will be completed the finalise the actual route. This is to indicate the proposed strategy only.*

NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Water

Water is separated into 2 streams – industrial and domestic

Industrial water refers to the water utilised for mechanical cooling. This will be fed from Lot 305 where the supply is a combination from Sydney Water and coNEXA's Aquanet Network Extension.

Additionally, fire services water supply is provided by on-site water tanks located on Lot 305.



Domestic water encompasses the water utilised for bathrooms, amenities, end of trips, kitchenettes, irrigation, cleaners points.

This will be drawn from the Sydney Water network and a separate application will be submitted to Sydney Water for a tap in specifically for Lot 306.



NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Water & Sewer

Water Demand

Water use across the development comprises industrial cooling water and domestic potable water.

Industrial water will be used primarily for mechanical cooling systems associated with the data halls, while potable water will service staff amenities and building facilities.

Industrial Water Demand

Industrial cooling water will be supplied via infrastructure located on Lot 305, drawing from a combined supply from:

- Sydney Water, and
- coNEXA's Aquanet recycled water network.

Development	Industrial Water Demand	Peak Flow
Lot 305 (Buildings A–D)	12,528,000 L/day	145 L/s
Lot 306 (Buildings E–G)	7,305,120 L/day	85 L/s
Total Campus Demand	19,833,120 L/day	229.55 L/s

Domestic Water Demand

Domestic water demand has been calculated based on an assumed consumption rate of 40 L/person/day for office and staff amenities. Potable water will be supplied via the existing Sydney Water main located in Burley Road, which currently services the S4 campus.

Development	Domestic Water Demand	Peak Flow
Lot 305	6,680 L/day	7.76 L/s
Lot 306	3,600 L/day	5.67 L/s
Total Campus Demand	10,280 L/day	7.76 L/s

NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Water & Sewer

Sewer Discharge

Wastewater generated by the development will consist primarily of domestic wastewater associated with staff amenities, with minimal wastewater generated from operational processes.

Based on the hydraulic assessment undertaken as part of the Sydney Water Section 73 servicing assessment, the estimated wastewater discharge associated with the development is as follows:

Wastewater will discharge from the private sanitary drainage system to the existing Sydney Water DN225 sewer main located near the western boundary of the site.

Hydraulic modelling undertaken for the development has confirmed that the existing DN225 sewer main has sufficient capacity to accommodate the proposed wastewater flows, with the network operating within acceptable capacity limits.


Accordingly, no amplification of the sewer network is required to service the development at this stage.

Parameter	Sewer Discharge
Maximum Discharge	938.5 kL/day
Average Discharge	797.7 kL/day
Peak Simultaneous Discharge	21.51 L/s

The proposed water and wastewater servicing strategy has been developed in consultation with Sydney Water and demonstrates that the development can be accommodated within the capacity of the existing authority infrastructure servicing the S4 campus.

NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Industrial Water

coNEXA Recycled Water Supply Extension (Aquanet Network) – Points of entry to site

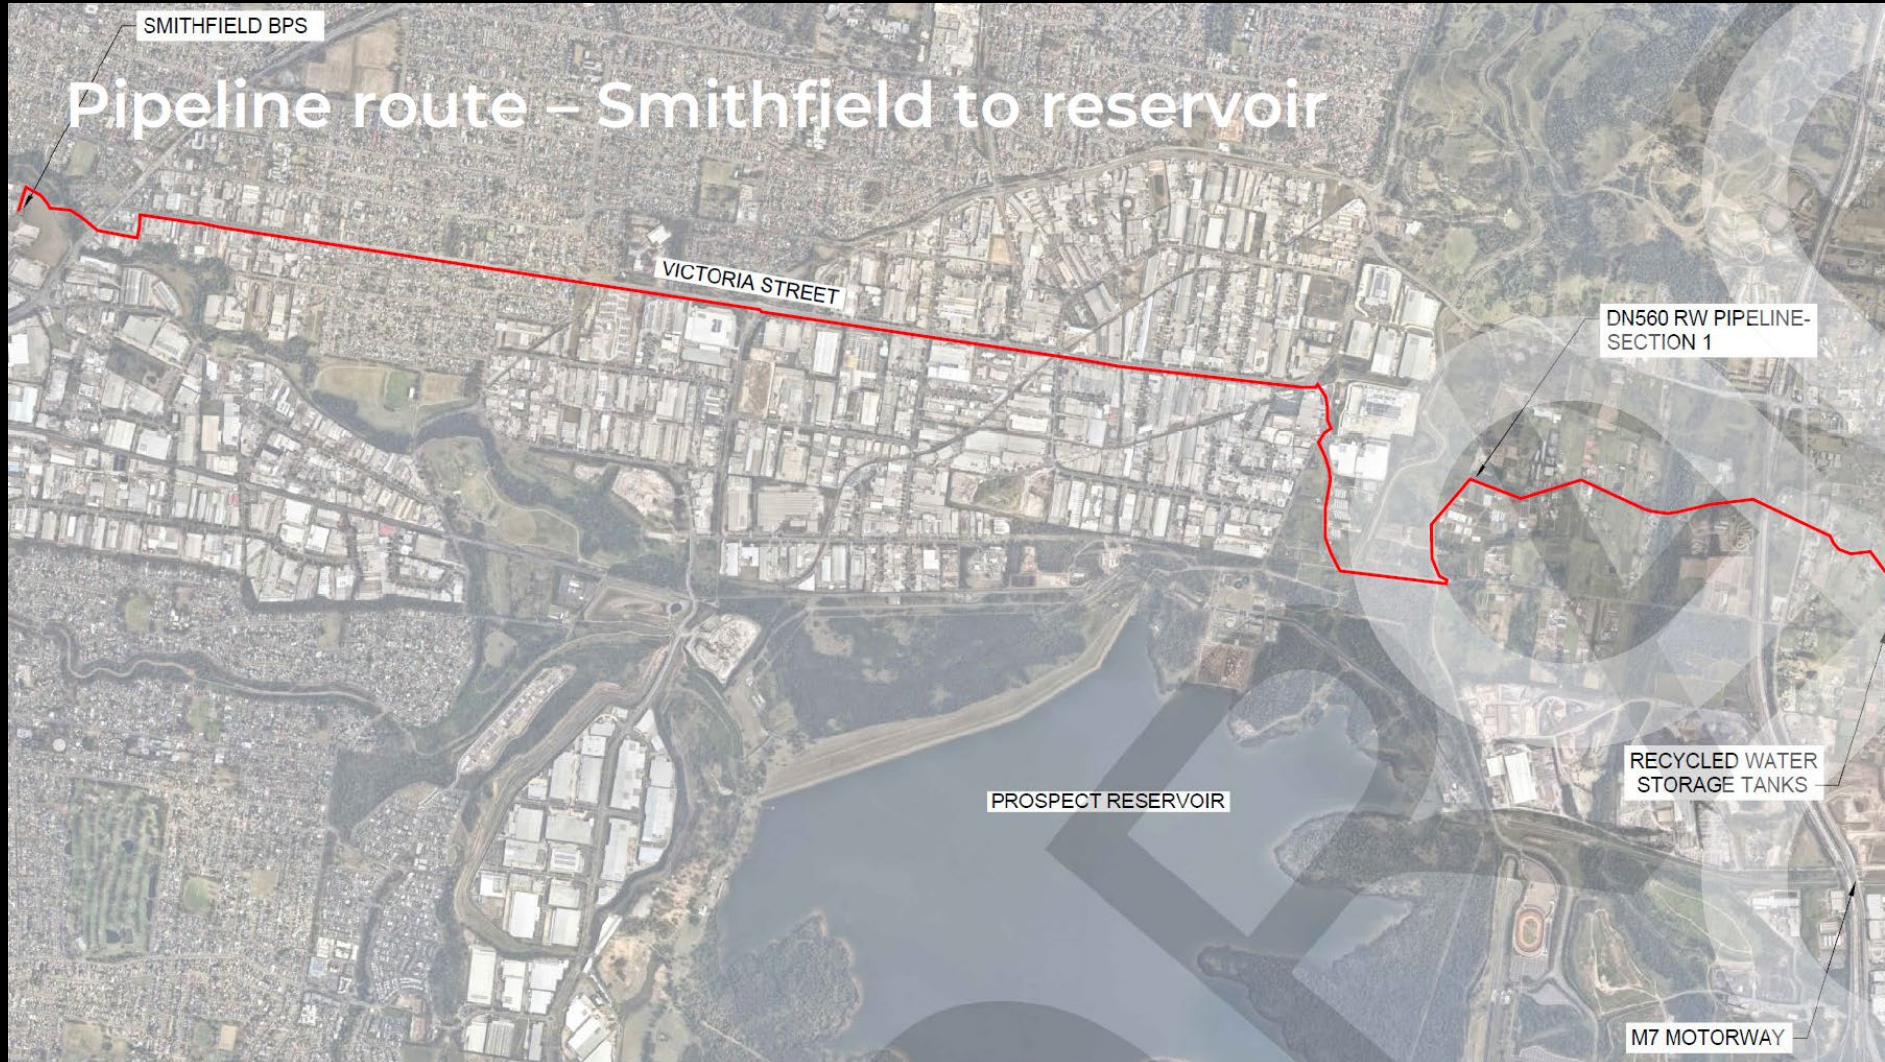


The external route runs approximately 10.5 km from AquaNet's Smithfield facility to the high-level reservoir site in Horsley Park. The alignment follows public roads and utility corridors, avoiding major infrastructure like the M7.

It has been selected to optimise constructability, minimise third-party impacts, and ensure reliable delivery to the reservoir, from which water gravity-feeds to the S4 site.


NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Industrial Water

coNEXA Recycled Water Supply Extension (Aquanet Network) – Points of entry to site

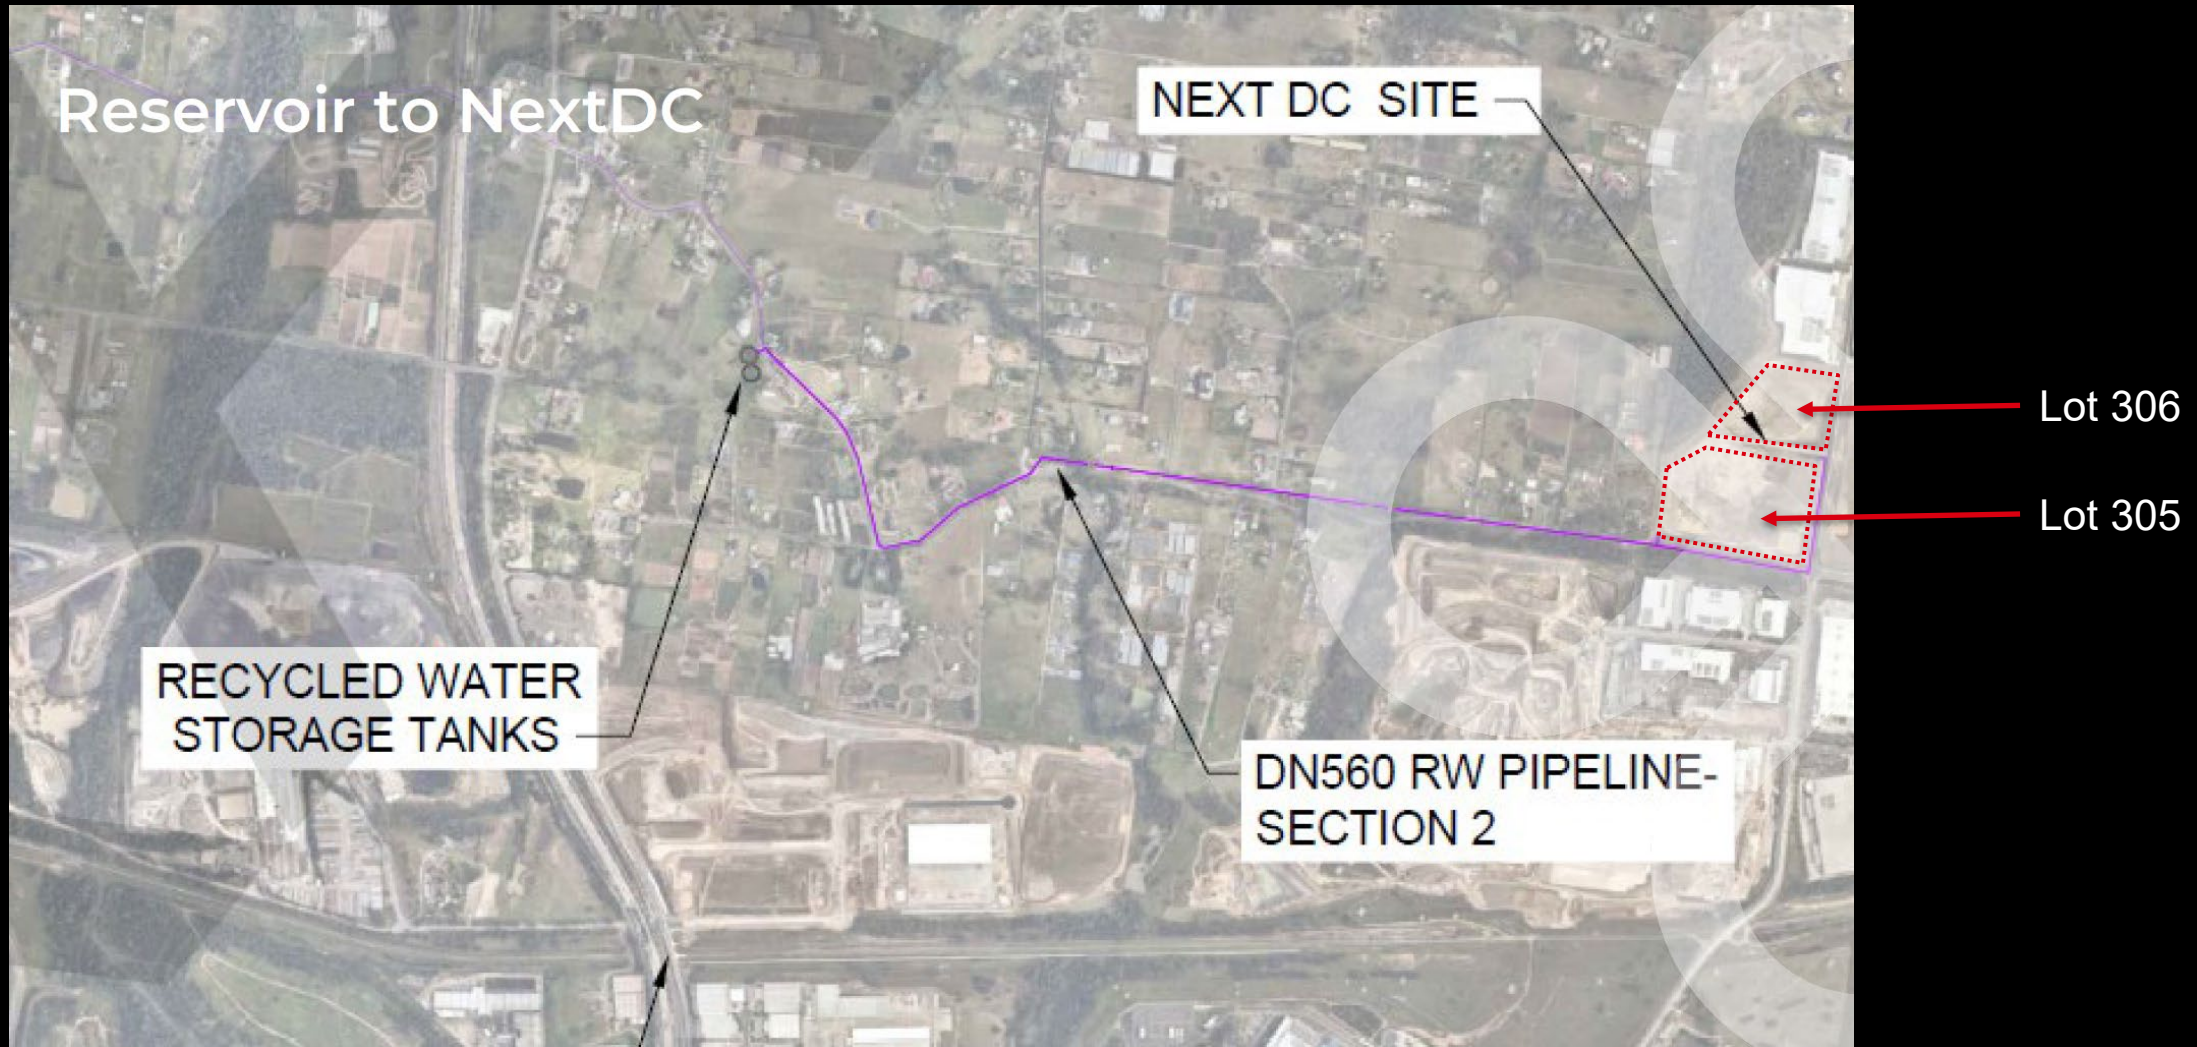

NEXTDC S4 Lot 306 | Infrastructure Servicing Strategy | Water

Points of entry to Lot 305

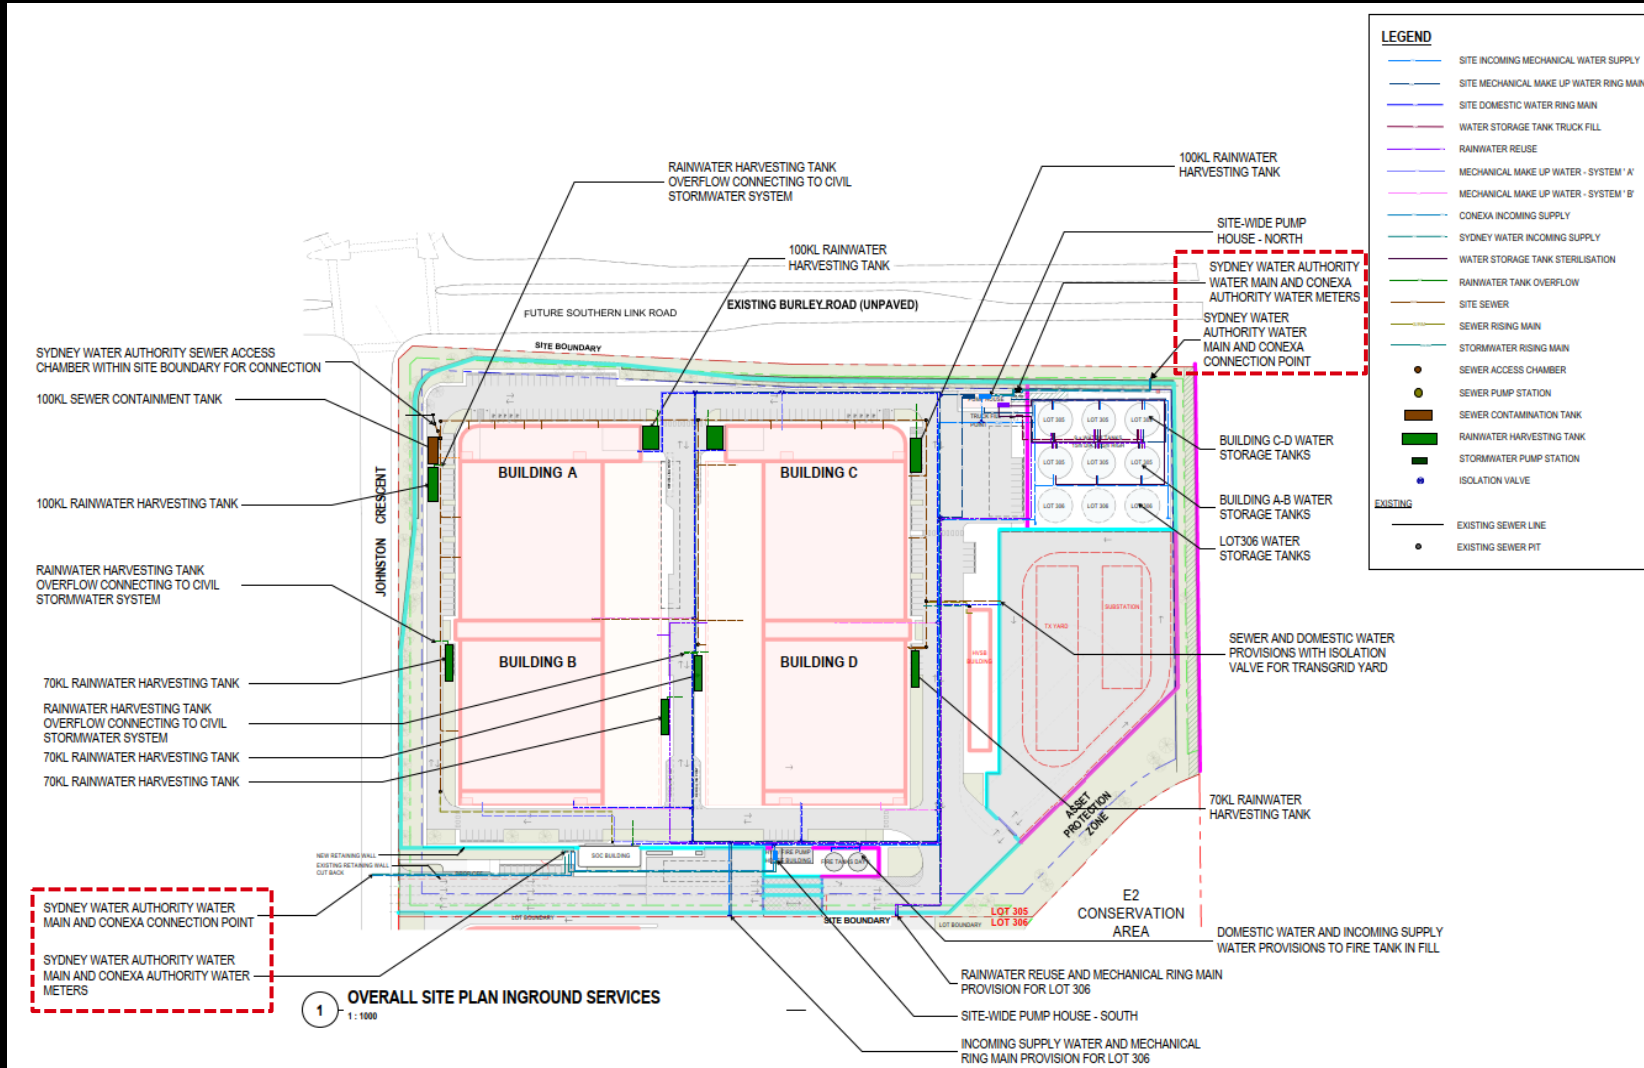


Potable water supply to the S4 site is via a Sydney Water Authority main, entering the site from Burley Road.

The connection point is co-located with the coNEXA supply interface and includes authority water meters within the site boundary.

This entry point serves as the primary interface for incoming potable water, linking to site-wide mechanical and domestic water ring mains.

Points of entry to Lot 306



The Orange line indicates supply to Lot 306 from an existing Sydney Water potable cold water main.

**all pathways indicated are conceptual only and further design development will be completed to finalise the actual route. This is to indicate the proposed strategy only.*

NEXTDC S4 Lot 306 | Infrastructure Adequacy Statement

Infrastructure Adequacy Statement

The proposed development has been designed to utilise the existing infrastructure established for the approved NEXTDC S4 campus, including electrical supply, recycled industrial water, potable water and sewer networks. The servicing strategy integrates the proposed development on Lot 306 with the existing infrastructure on Lot 305, allowing utilities to be distributed across the campus through established connections and infrastructure corridors.

Electrical supply will be provided via the NEXTDC dedicated substation connected to the Transgrid Sydney West Substation, with a total available capacity of 500 MVA across the campus. The proposed development operates within the allocated electrical capacity and does not require additional power supply upgrades.

Industrial cooling water will be supplied through the coNEXA recycled water network and Sydney Water supply infrastructure, while potable water will be sourced from the existing Sydney Water main located in Burley Road. Wastewater generated by the development will discharge to the existing Sydney Water DN225 sewer main, which has been confirmed through hydraulic assessment to have sufficient capacity to accommodate the proposed flows.

Based on the investigations undertaken to date, the proposed development can be serviced by the existing and approved infrastructure networks associated with the S4 campus, and the development is not expected to require significant off-site infrastructure upgrades during the operational phase.
